Top Technical Failures: Power & Redundancy

Issue: MW Equipment Power Redundancy mismatch (448 instances)

Requirement: Two different power sources to MW & BTS racks (Separate Circuit Breakers).

QC Findings:

- Wrong Photo: **407**
- No multiple sources for MW & BTS: **32**
- Missing photo: **9**

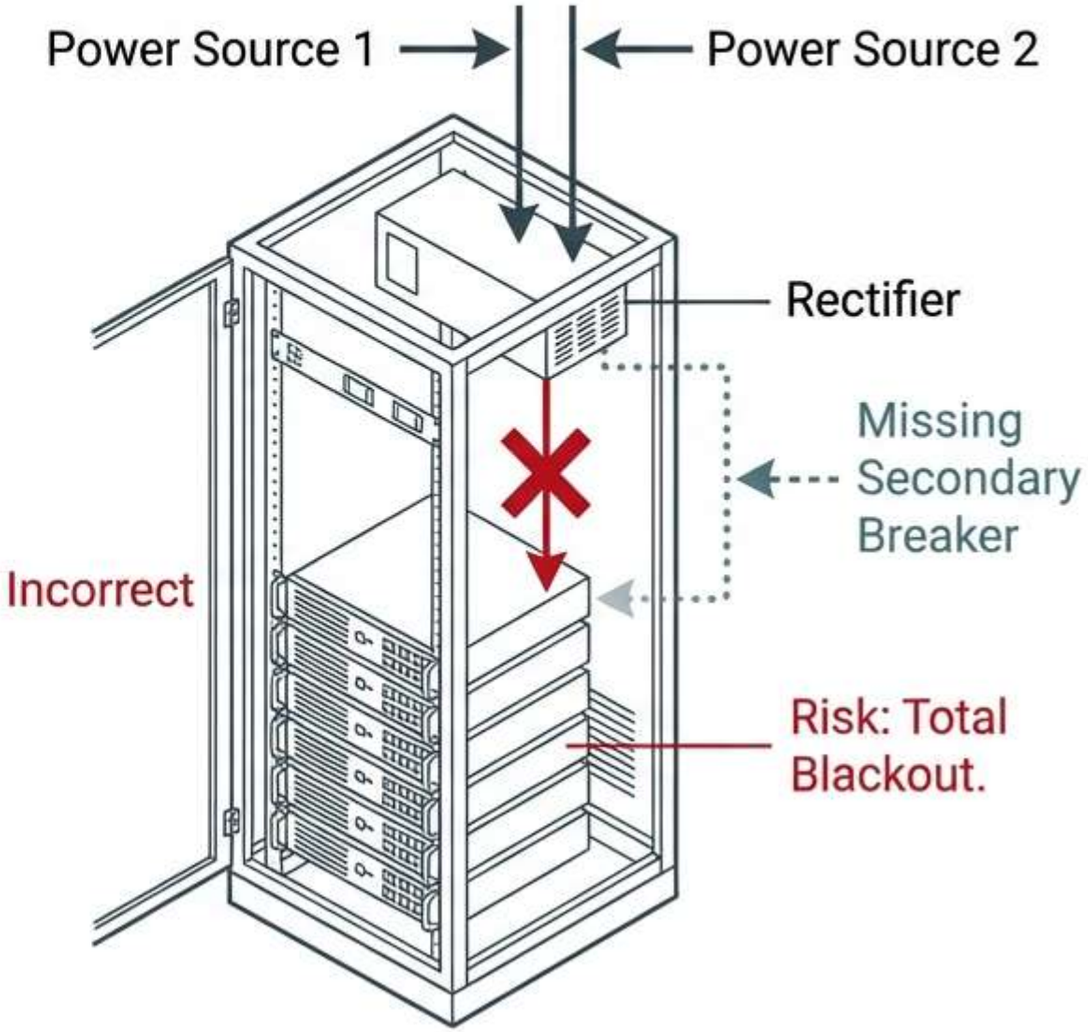

The Field Reporting Integrity Gap

REPORTED STATUS (FME)

99.5% OK

FME claims near-perfect compliance.

DATA MISMATCH

AUDITED REALITY (QC)

27.1% NOK

Audit reveals significant failure rate.

"FME has responded to all PMR checklist items as OK regardless of actual site status."

Top Technical Failures: Grounding & Safety

Issue: Main Grounding & Earthing Pit connections (434 mismatches)

Requirement: Connection to Earthing Pit, Rod, and Bus Bars.

QC Findings:
- No earth connected Bar: **362**
(Critical Safety Risk)
- Wrong Photo: **59**

Secondary Issues:
- RF Antennas Grounding: 327 mismatches
- MW ODUs Grounding: 270 mismatches

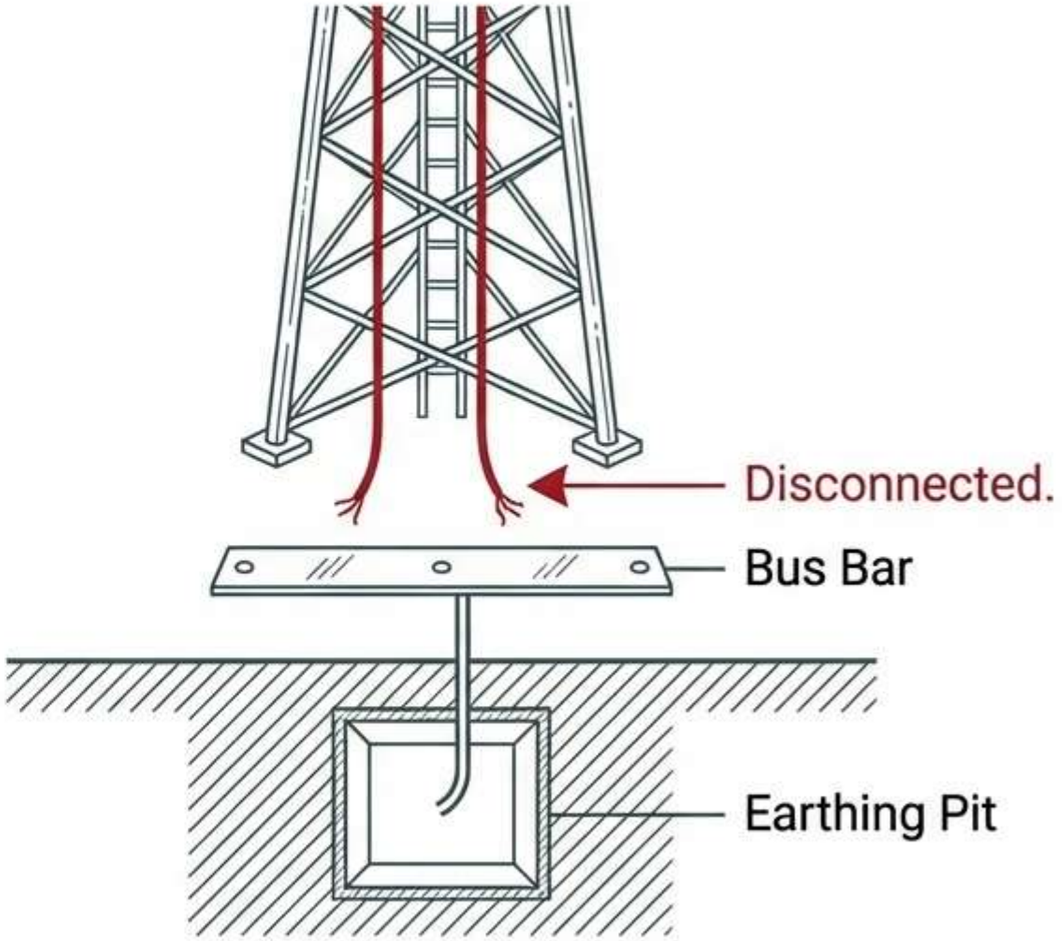

Risk: Equipment Damage & Safety Hazard.

Analysis of QC Rejections
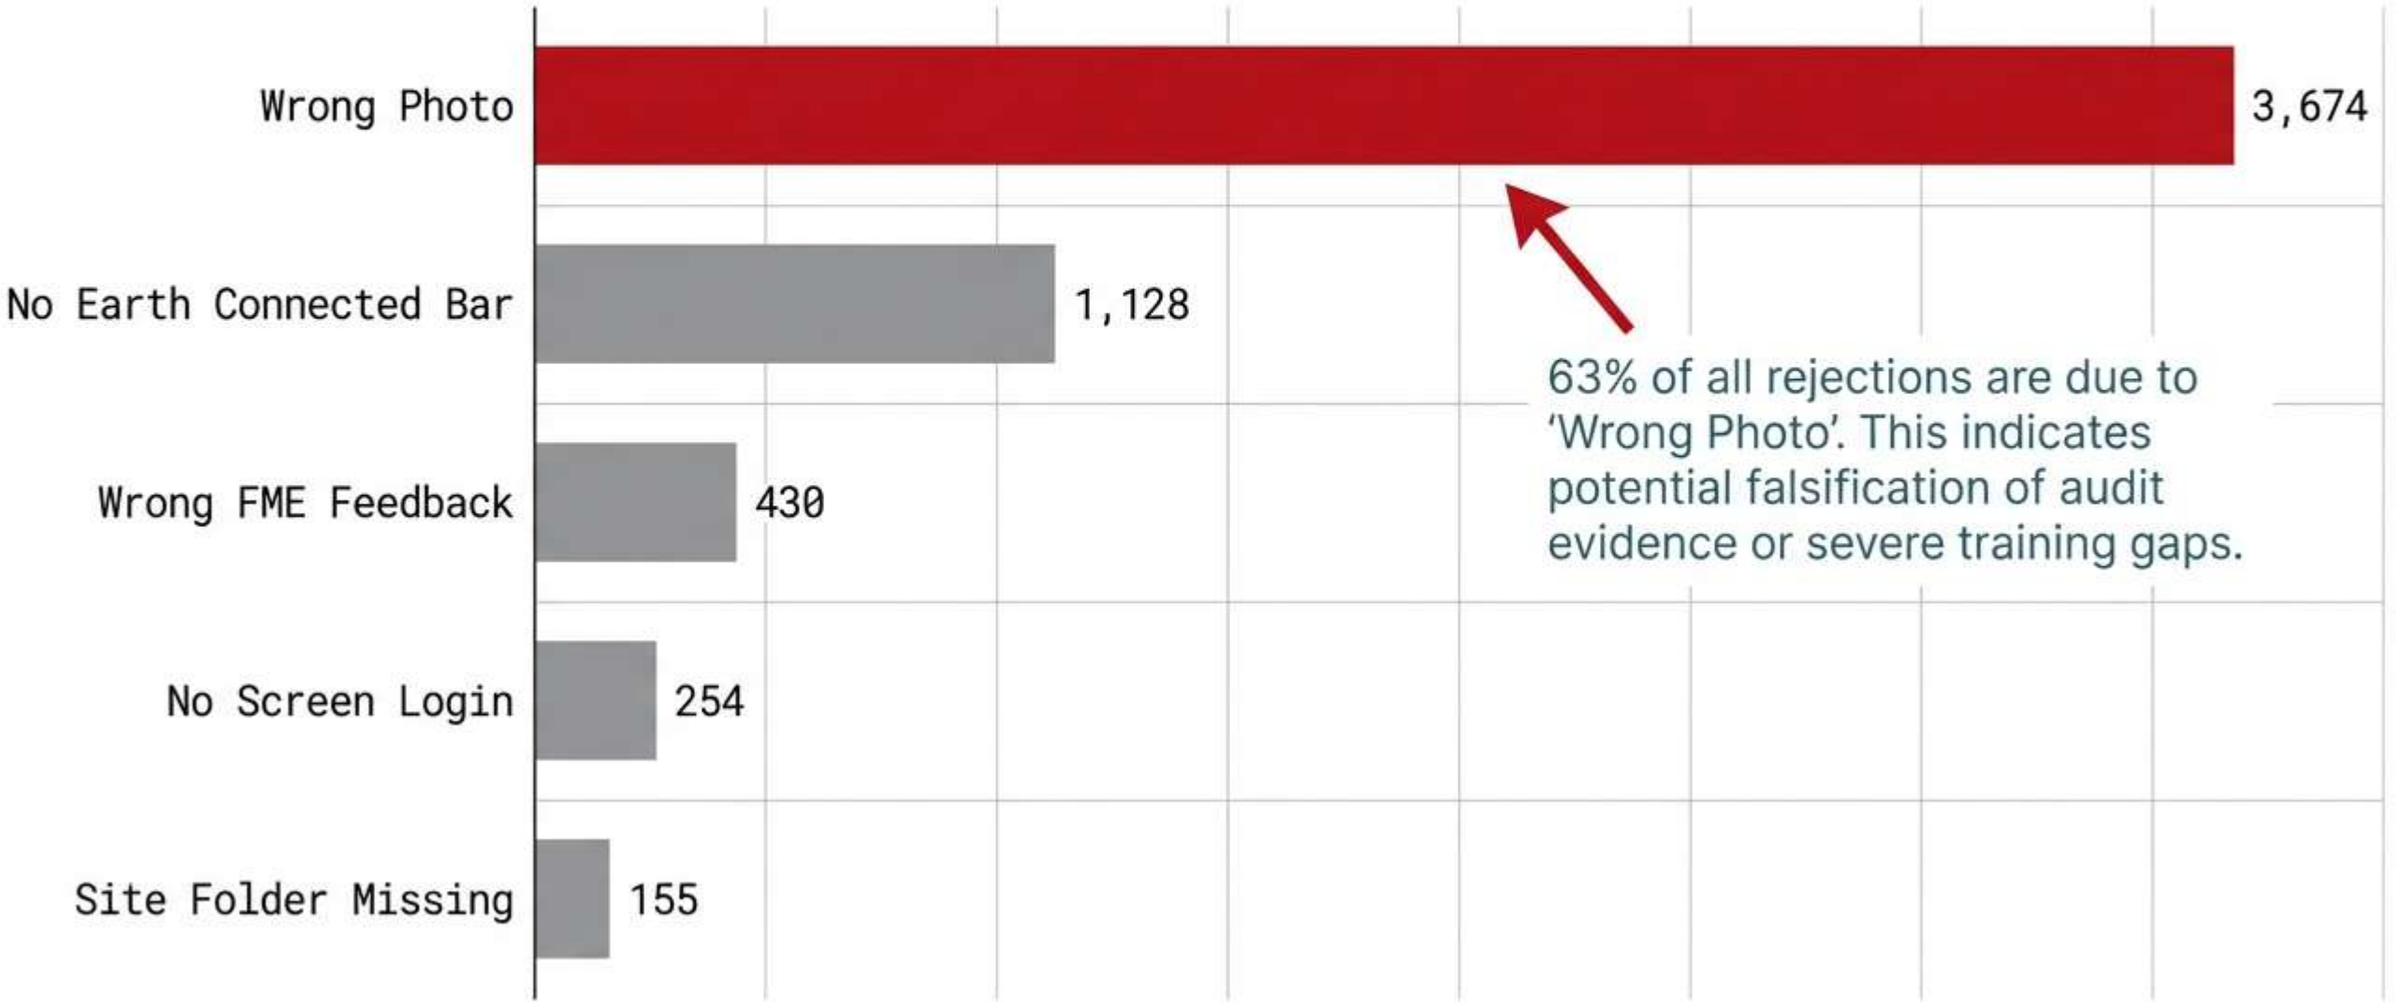
Why were the field reports rejected?
